



Weekly Progress Report for:

Missoula Mercantile Deconstruction

17-7510

Week Of:

March 31, 2017



Missoula Mercantile Project

Weekly Report-3-27-17

Deconstruction Phase

On-Site Activity:

MONDAY-3-27-17

1. Monday morning March 27th. A load of material leaving the site this early Monday morning. There will be five loads being moved off site today.
2. This is a stack of that material out in the parking lot staging area. All of this will be loaded onto trucks and trailers and removed from the site today.
3. Remember that old radiator that was in the elevator shaft on the second floor. Pictured here, as I was able to get a little closer. This is it just before it was removed.
4. Here it is on a pallet and it took 5 crewmembers to get this on to that pallet. We didn't find any names or numbers on it. We estimated it weighs about 600 pounds, now we know why it was left there. Thank goodness for central heating and air.
5. This is a beautiful wood bifold door. I would say that it's probably original to the building. This has been removed along with the door shutters, and will be stored at Home ReSource.
6. North side of the building void of most of the metal clad window shutters and doors.
7. The shutters have been stacked here in the lot along with the rails and the guidepost. All of this is being retrieved so that it can be reused at a later date.
8. These large cast wheels came from the top of the old freight elevator. These at one time probably had some sort of cabling and electric motor attached. They were abandoned in place, now they have been salvaged.



Missoula Mercantile Project

Weekly Report-3-20-17

Deconstruction Phase

On-Site Activity:

TUESDAY: 3-28-17

1. North side of the building, all of the shutter on the doors and windows have been removed. There is a section of bars on the window to the left, bottom. These will be taken off and saved also.
2. This picture is one of the sets of bars that we were able to actually save intact.
3. This is the window on the north side of the building. All of the bars have been removed by others.
4. These metal clad shutters both for the window and the doors were moved inside. Soon to be loaded up this week and take it over to HR.
5. The crew is working on the decorative canopy on the main entrance. This is coming off in sections. This is all copper, and every piece will be numbered and saved. To be reassembled somewhere of importance at a later date
6. Another angle showing the configuration of the half circle canopy over the entrance. Picture shows that someone else removed most of the steel bars that were over the bottom floor windows. We were able to save one complete.
7. This is one of the glass panels, there tapered into a pie shape. The configuration are actually two panes of glass. One is clear that is on the bottom, the other one is waffled which is on the top.
8. This item right here is a bollard it was placed on the corner of the building along the alleyway in order to protect the brick masonry. If you ran into one of these, you certainly had a dented up fender. There's one more of these on the inside, in the area that was designated as the loading dock.



Missoula Mercantile Project

Weekly Report-3-20-17

Deconstruction Phase

On-Site Activity:

Wednesday: 3-29-17

1. The crew is starting work on the removal of the decorative copper canopy at the main entrance to the Mercantile.
2. Can you say a trailer load of radiators, yes you can. All shapes and sizes different configurations. And very heavy.
3. The last load of salvageable wood material to leave the site. The next phase of demolition will produce the post and beam that will be removed by the demolition contractor. These two will be salvaged and taken to Home ReSource.
4. These are the metal clad window and door shutters. Being prep to be loaded onto the trailer and taken to HR for storage
5. A box containing various pieces of hardware removed from the joists within the building. These two will have value, because these are all hand forged steel.
6. The crew working on taking the banister rails off the interior staircase.
7. The crew continuing to work on taking the decorative copper entrance apart. There are quite a few pieces involved in this work of art.
8. The two cast-iron bollards have been united at long last.



Missoula Mercantile Project

Weekly Report-3-20-17

Deconstruction Phase

On-Site Activity:

Thursday: 3-30-17

1. The crew is working on the decorative canopy on the front of the building they're in the process of removing this.
2. This part of that decorative canopy the half round part that had the glass in. This has been unbolted from the building. It is in the process of being lowered to the ground.
3. It took 10 guys to pick this half circle of iron and copper up. They are placing it on a flatbed trailer. It will be moved right away to HR. for storage.
4. This just barely did fit on an 8 foot trailer. It'll be strap down gingerly, and removed from the site today. It will be at HR. waiting for a new home.
5. This trailer has been loaded with a lot of the salvaged item you can see the two bollards. Those are the wheels from the old freight elevator. Also the curled rolled up doors which were in the receiving area. All being stored at HR.
6. These are the bricks that were taken from the Archway in the basement that had notable dates and signatures.
7. The upper part of the decorative copper work at the front elevation. The crew indicates to me that they believe they can take this entire decorative scroll work off in one piece. That would be awesome.
8. Another trailer loaded both with salvage items and tools. The pallet that you see to the left at the front of the trailer is the stack of decorative leaded glass. That came from the front of the store along Higgins Street.





CONSTRUCTION

Missoula Mercantile Project

Weekly Report-3-20-17

Destruction Phase

On-Site Activity:

Friday 3-31-17

1. This is the last section of the decorative copper entryway into the Mercantile. This is the section that we hope will come off all in one piece.
2. They have it strapped and supported and they are working on prying it away from the masonry.
3. Yes it did come away in one piece. We're not quite sure why it was still attached to the building. It was probably being held up by force of will.
4. Now sitting on the trailer ready to be transported to storage. Hopefully for a new home and a new life to be reunited with the other parts of the decorative entryway of the Missoula Mercantile.
5. All the other parts and pieces wrapped marked and ready to go.
6. Now you see it as it stood here in all its glory for many, many years. Remember that this is copper it was Penny bright when it was installed. Over the years as copper does it fades into a greenish patina. I hope that someday when it's all re-assembled in a place somewhere inside out of the weather. That it can be brought back to that Penny brightness. I hope I get to see that someday.
7. Now it's gone. Taking down put in storage. This is very much what the installer would've seen when he came to actually install his work of art. His masterpiece those many many years ago.
8. Yes the time has come. Its demobilization day Friday, March 31. All of Heritage Timber and Home ReSource crews have demobilized. Moved off the site. The demo phase will start on Monday, April 3.

#1.



#2.



#3.



#4.



#5.



#6.



#7.



#8.





Missoula Mercantile Project

DAILY SALVAGED MATERIAL

Friday-2-17-17

Materials: Wood Removed

60- 2" x 8' x 20' rough cut	60-2" x 8" x 12' rough cut	12- 4" x 6" x 20' rough cut
3- 4" x 6" x 16' rough cut	2- 4" x 6" x 7' rough cut	

Monday-2-20-17

Materials: Wood Removed

74-1" x 6" x 14' rough cut	14-2' x 12" x 19' true cut	86- 1' x 6" x 8' rough cut
43-2" x 8" x 12' true cut	30- 2" x 8" x 19' true cut	14-2' x 12" x 19' true cut
14-2" x 12" x 8' true cut		

Tuesday-2-21-17

Materials: Wood Removed

130-2" x 8" x 14' true dimension		
40-2" x 8" x 17' true dimension	40-2" x 8" x 17' true dimension	50-2" x 8" x 12' true dimension

Wednesday- 2-22-17

Materials: Wood Removed

186-1" x 6" x 20' rough cut	64- 1" x 8" x 14' rough cut	24- 4" x 4" x 8' rough cut
-----------------------------	-----------------------------	----------------------------

Thursday-2-23-17

Materials: Wood Removed

119- 2" X 6" X 20'	2- 2" X 8" X 15'	2-2" X 8" X 20'
14- 2" X 12" X 26'	2-2" X 8" X 13'	4-2" X 8" X 20'
4-2" X 12" X 16'	2-2" X 8" X 14'	

FRIDAY-2-24-17

Materials: Wood Removed

176-1" X 6" X 10'	76-1" X 6" X 14'	64-1" X 6" X 16'
42- 1" X 6" X 10'	76- 1" X 6" X 15'	28- 1" X 6" X 12'





Missoula Mercantile Project

DAILY SALVAGED MATERIAL

Monday—2-27-17

Materials: Wood Removed

2-2"x 6"x 4'	2-2"x 6"x 2'	2-2"x 6"x 7'	3-2"x 6" x 8'	6-2"x 6"x 10'
2-4"x 6"x 8'	2-4"x 6"x 8'	2-4"x 6"x 8'	11-2"x 8"x 9'	13-2"x 8"x 6'
9-2" x 8"x7'	7-2"x 8"x 8'	6-2"x 8"x 12'	2"x 8"x 12'	8-2"x 8"x 15'
6-2"x 8"x 17'	1-2"x 8"x 18	1-2"x 8"x 18'	1-2"x 8"x 23'	6-1"x 12"x 13'
4-2"x 10"x 10'	6-1"x 10"x 12'	5-1"x 10"x 12'	8-2'x 4"x 12'	16-2"x 4"x 8'
5-1"x 12'x 14'	6-2"x 4"x 6'	6-2"x 4"x 12'	140-1"x 6"x 12'	

Tuesday—2-28-17

Materials: Wood Removed

140-1"x 6'x 9'	98-1"x 6"x 5'	112-1"x 6" x 5'	96-1"x 6"x 6'	50-1"x 6"x 5'
38-1"x 6"x 7'	4-1"x 6" 6'	4-1"x 6"x 4'	5-1" x 6"x 8'	2-1"x 6" x9'
1-1"x 6"x10'	5-1"x 6"x 13'	1-1"x 6'x 14'	2-1"x 6'x 15'	6-1"x 8'x6'
14-1'x 8'x10'	40-2'x 8'x 1			

Wednesday 3-01-17

Materials: Wood Removed

160-1" x 6' x 14'	30-2" x 4" x 8'
-------------------	-----------------

Thursday-3-02-17

Materials: Wood Removed

40-2"x 6"x 24'	10-2"x 6"x 14'	10-2"x 6"x 8'	50-2"x 6"x 14'	22-2"x 6"x 16'
36-2'x 4"x 8'	42-2"x 4'x 5'	10-2" x 4'x 6'	30-2"x 4"x 8'	44-2" x 6"x 10'
120-2"x 6"x 10'	74-2"x 6"x 18'			

FRIDAY-3-03-17

Materials: Wood Removed

77-1"x 6"x 8'	20-1"x 6"x 4'	38-2"x 6"x 6'	27-2"x 4"x 8'	18-2"x 12"x 25'
18-2"x 12"x 20'	24-2'x 12'x 20'	16-2' x 12"x 14'	52-2'x 4"x 10'	40-1"x 6"x 6'
3-4"x 6"x 14'	12-2"x 12"x 15'			





Missoula Mercantile Project

DAILY SALVAGED MATERIAL

Monday—3-06-17

Materials: Wood Removed

66-2' x 8" x 12'	55-2" x 6" x 7'	18-2" x 6" x 4'	20- 2" x 12" x 14'	20-2' x 12" x 10'
30-2" x 12' x 25'	20-2" x 12" x 20'	30-2' x 12' x 20'	106-1' x 6' x 6'	

Tuesday—3-07-17

Materials: Wood Removed

24- 2' x 12' x 24'	54-2' x 12' x 20'	18-2" x 12' x 27'	46-4" x 4" x 5'	47-1" x 6" x 7"
--------------------	-------------------	-------------------	-----------------	-----------------

FRIDAY-3-10-17

Materials: Wood Removed

24-2" x 4" x 12'	140-1" x 6"tg. X 16'	8-4" x 6" x 16'	60-1" x 10" x 12'
------------------	----------------------	-----------------	-------------------

Tuesday—3-14-17

Materials: Wood Removed

144-1" x 6" x 10'	52-1" x 6" x 18'	134-1" x 6' x 10'	240-1" x 6" x 10' T&G
108-1" x 6" 9' T&G			

FRIDAY-3-17-17

Materials: Wood Removed

24-2' x 16" x 22'	42-2 x 12 x 17'	160-1' x 6" x 10' T&G	120-1" x 6" x 10' RC
-------------------	-----------------	-----------------------	----------------------

Monday 3-20-17

Materials: Wood Removed

18-2' X 16" X 25'	6-3" X 16" X 23'	46-2" X 12" X 12'	108-1' X 6' X 12'	39-2' X 12" X 19
-------------------	------------------	-------------------	-------------------	------------------

Wednesday 3-22-17

Materials: Wood Removed

55-2" x 14' x 19'	5-2" x 10" x 16'	3-4" x 6" x 12'	23-3' x 12" x 26'	120-1" x 8" x 12'
90-1" x 6" x 12'	110-1" x 8" x 6'			





Missoula Mercantile Project

DAILY SALVAGED MATERIAL

Thursday-3-23-17

Materials: Wood Removed

57-2" x 14" x 9' 20-2" x 14" x 23' 130-1" x 8" x 14' 33-2" x 14" x 10' 150-1" x 6" x 14'
4-4" x 4" x 8' 17-3" x 16" x 22' 1-3" x 16" x 27'

FRIDAY-3-24-17

Materials: Wood Removed

50-2" X 6" X 10' 88-2" X 10" X 12' 86-2" X 10" X 10'


Monday 3-27-17

Materials: Wood Removed

62-2' x 4" x 8' 100-1" x 10" x 10' 37-3" x 12" x 18' 50-1" x 6" x 8' 144-1" x 12" x 8' 29-2" x 15" x 9'
90-2" x 14" x 4'





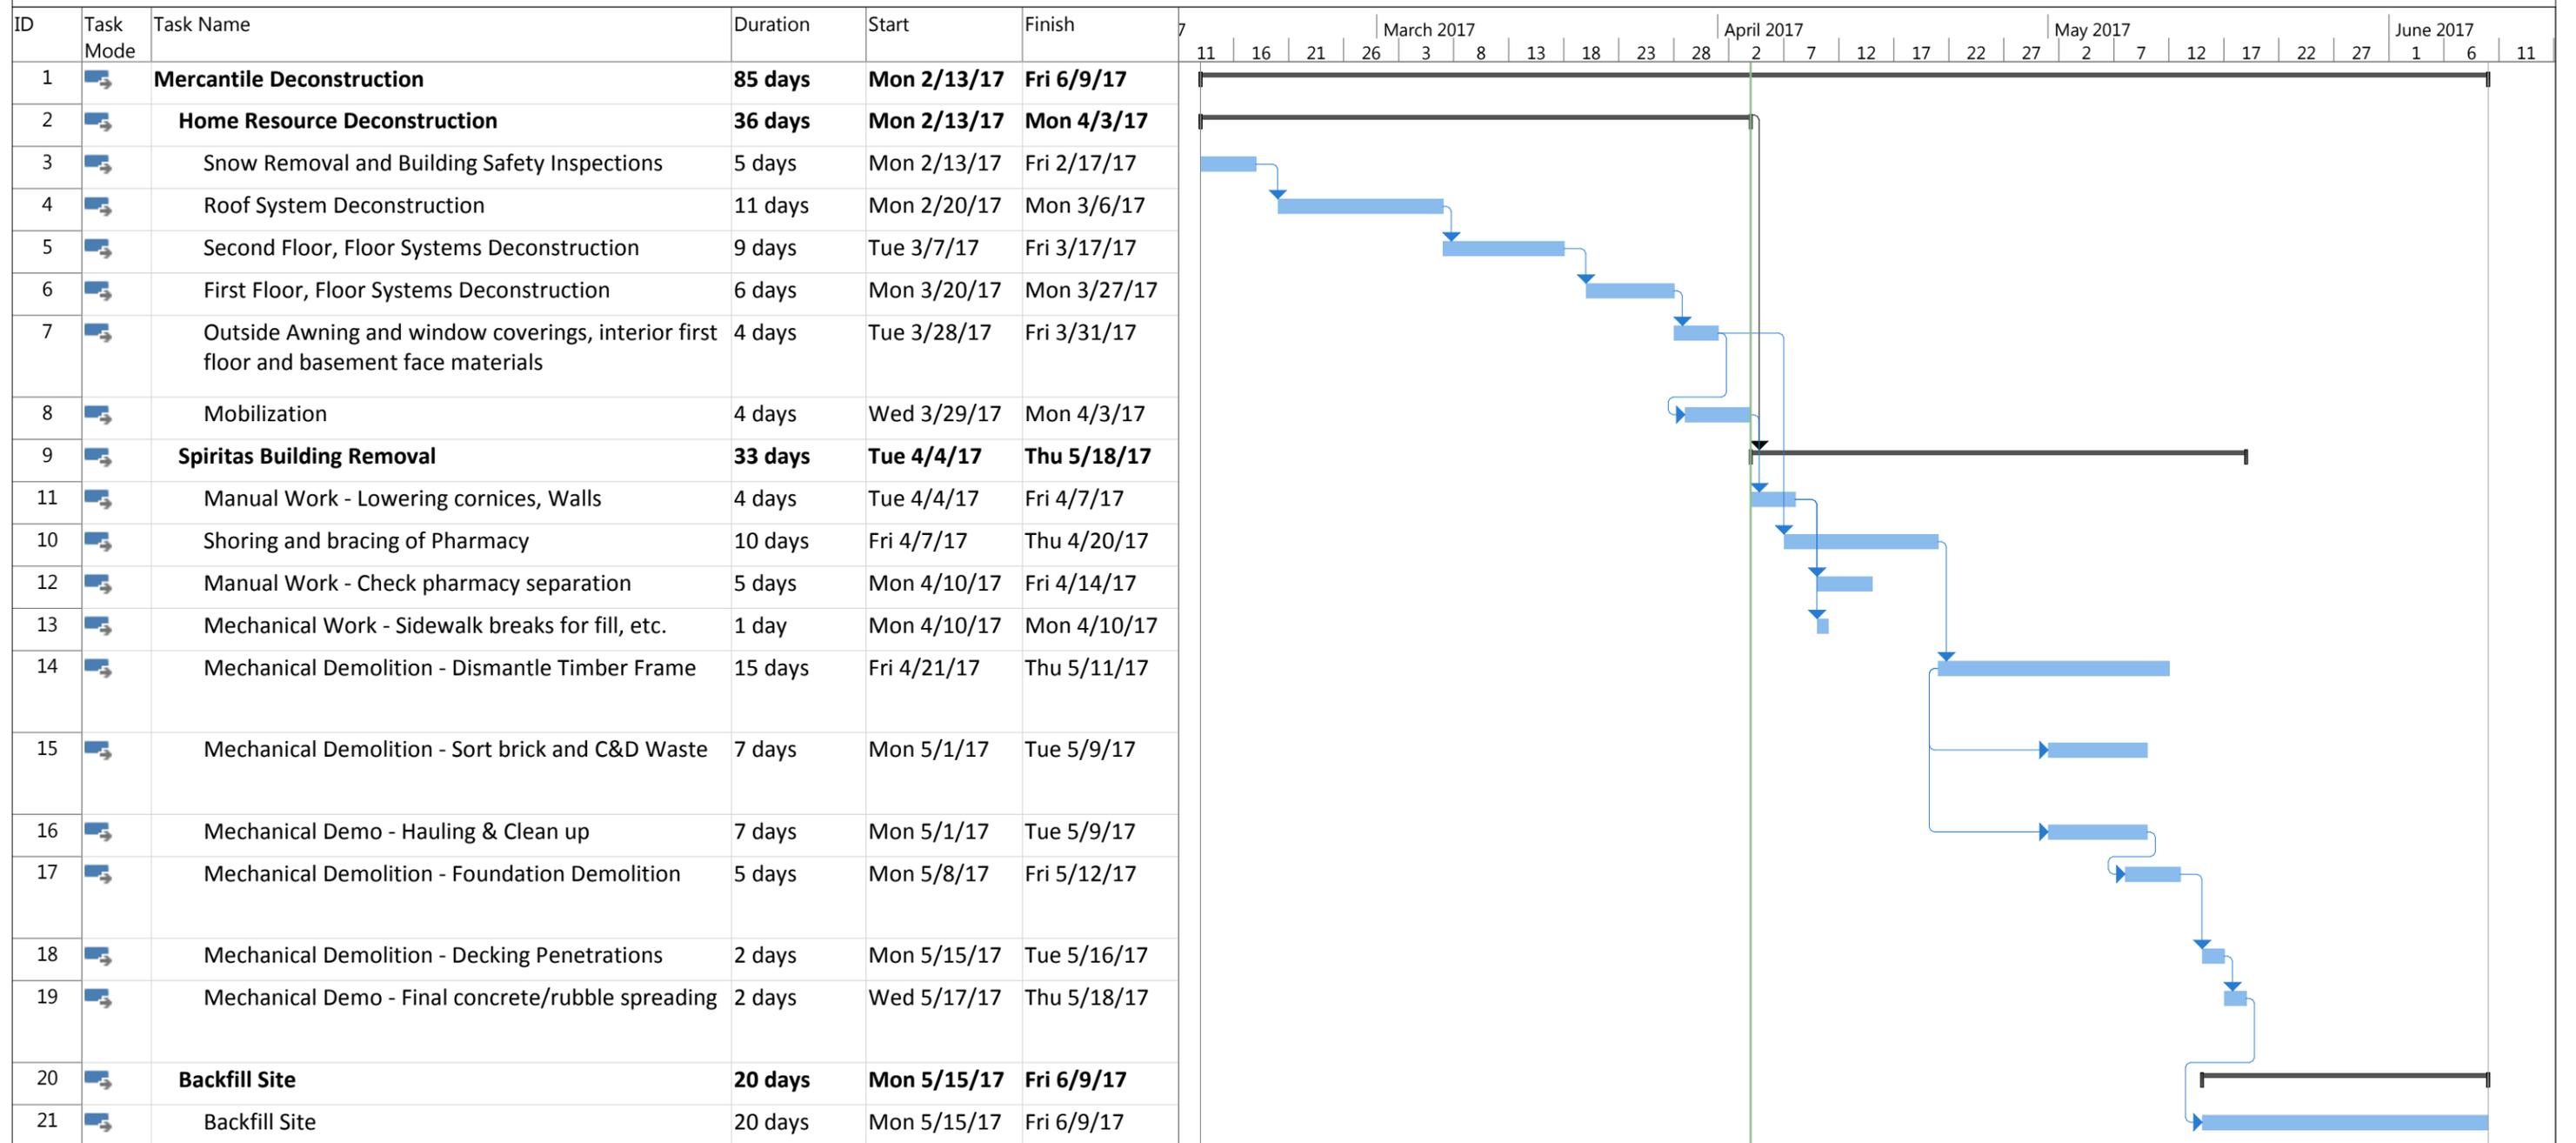

Project: Mercantile Date: Tue 4/4/17	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			
